Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Project: Automated Rubric Assignment Evaluator (key: ARAE) | Reporter: Hithashree S

Sprint: ARAE Sprint 1 (26 Aug 2026 to 2 Sep 2026, 1 week) | Estimation field: Story points

1. Epics

The Lab 1 functional requirements were grouped into five Epics, shown below in the Jira List view.

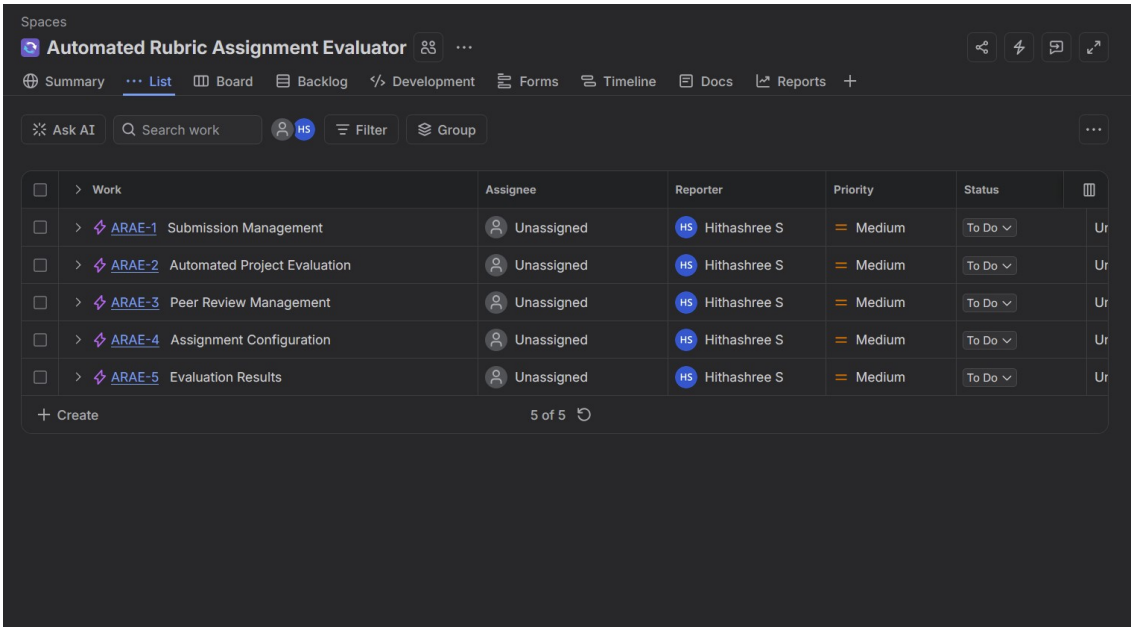


Figure 1: Epics ARAE-1 to ARAE-5 in the project List view.

Epic	Name	User stories	Story points
ARAE-1	Submission Management	ARAE-6, ARAE-7	8
ARAE-2	Automated Project Evaluation	ARAE-8, ARAE-9, ARAE-10	13
ARAE-3	Peer Review Management	ARAE-12, ARAE-13	8
ARAE-4	Assignment Configuration	ARAE-14, ARAE-15	8
ARAE-5	Evaluation Results	ARAE-11	5
	Total	**10 stories**	**42**

2. Backlog with User Stories and Story Points

Ten user stories were created under the Epics, prioritised, and estimated using the Fibonacci scale (3 and 5 points). The backlog totals 42 story points.

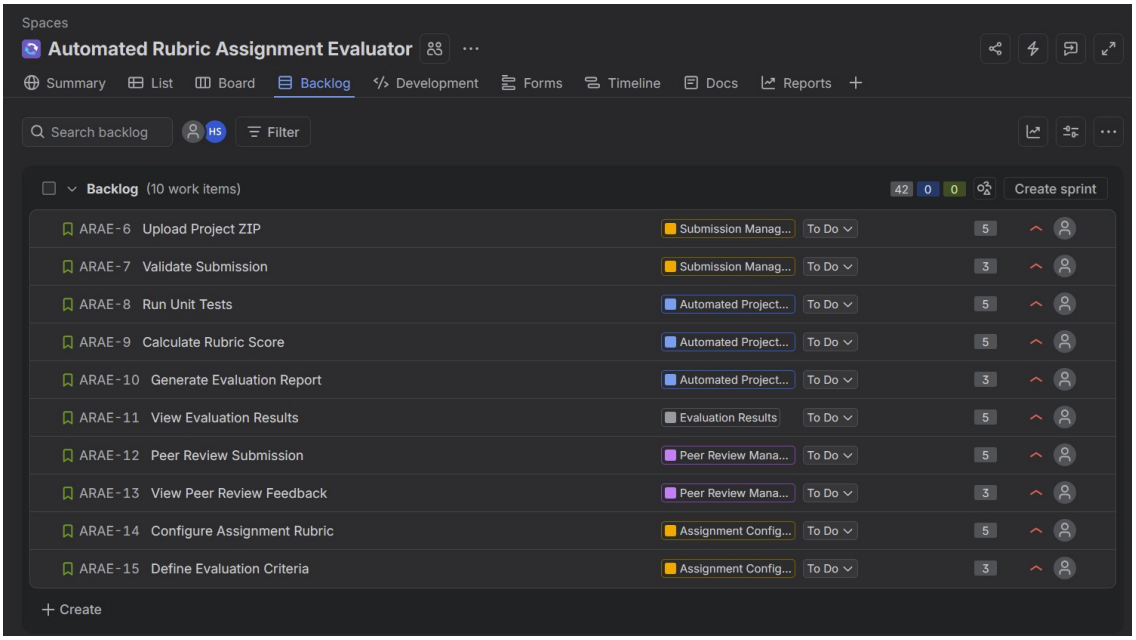


Figure 2: Product backlog showing stories, parent Epics, story points and priority.

Key	User story	Epic	Points
ARAE-6	Upload Project ZIP	Submission Management	5
ARAE-7	Validate Submission	Submission Management	3
ARAE-8	Run Unit Tests	Automated Project Evaluation	5
ARAE-9	Calculate Rubric Score	Automated Project Evaluation	5
ARAE-10	Generate Evaluation Report	Automated Project Evaluation	3
ARAE-11	View Evaluation Results	Evaluation Results	5
ARAE-12	Peer Review Submission	Peer Review Management	5
ARAE-13	View Peer Review Feedback	Peer Review Management	3
ARAE-14	Configure Assignment Rubric	Assignment Configuration	5
ARAE-15	Define Evaluation Criteria	Assignment Configuration	3

3. Sprint Board (Active Sprint View)

All selected stories were moved through To Do, In Progress and In Review, and finally to Done. The board shows 10 items in the Done column.

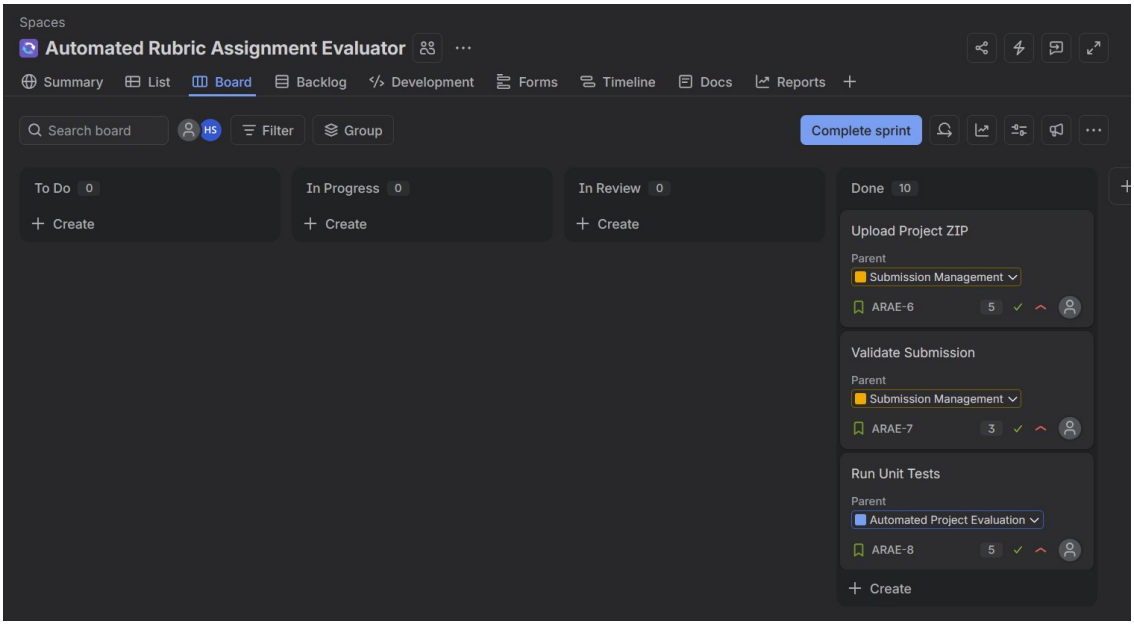


Figure 3: Sprint board with completed stories in the Done column.

4. Burndown Chart

The chart below is for ARAE Sprint 1, using story points as the estimation field. The sprint begins with 42 story points of remaining work, and the guideline (ideal burn rate) falls to 0 by 2 September.

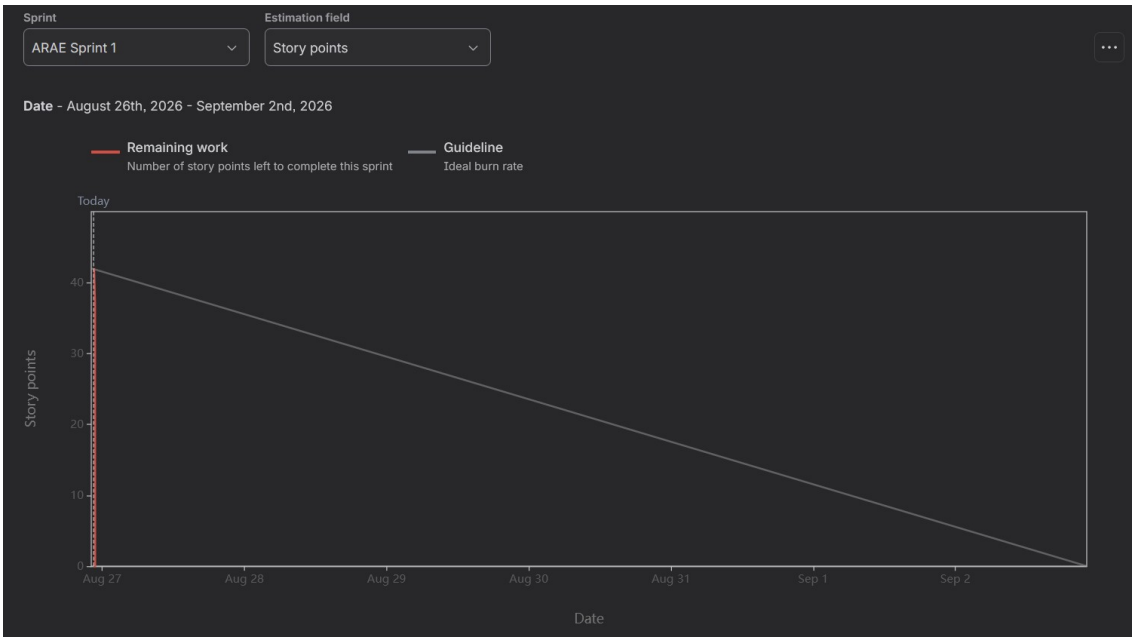


Figure 4: Sprint burndown chart (remaining work vs. guideline).

5. Reflection

1. Did your estimations reflect the actual effort?

Yes, I feel that the estimations were fairly close to the effort required for the tasks. I assigned 3 or 5 story points based on how difficult I felt each user story would be. Since I was able to complete all the planned stories in the sprint, the estimation was reasonable. However, because this was a simulated sprint, I did not record the actual time taken for each task.

2. Was your backlog well-prioritised?

Yes, I think my backlog was reasonably prioritised. I arranged the stories based on the flow of the system, starting with submission-related tasks and then moving towards evaluation, results, peer review and assignment configuration. This made the backlog easier to work with. I could have made the priority differences clearer by assigning different priority levels to the stories instead of keeping many of them similar.

3. How did your simulated sprint align with your plan?

The sprint aligned well with my plan. I had planned to complete all 10 user stories, with a total of 42 story points, in the one-week sprint. I moved the stories through the different stages in the Jira board and completed all of them. Since it was a simulation, the tasks were completed much faster than they would normally be in a real development sprint.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart helped me understand how the work was progressing during the sprint. I started with 42 story points and the ideal burn rate was around 6 points per day. Since I completed the stories quickly in the simulation, the remaining work decreased faster than the ideal guideline. It showed me how the burndown chart can be used to track progress and compare the completed work with the planned sprint work.
